


January 2016 - Current Proposal

- 1) Escalators installed + commissioned as per Crossrail design. Handover to CoL
- 2) Moorgate LUL ticket hall demolition commences JUNE 2015
- 3) 21 MF hoarding up + Demolition in progress HIGHWALK CLOSED (from June 2015)

Implications

- A) Escalators are blocked until 21 MF project completion Jan 2019
- B) 1 Year warranty on Escalators commences
- C) Escalators installed to incorrect levels and spec for permanent condition and therefore need to be replaced
- D) Escalators aesthetically unsuitable for permanent condition


21 Moorfields - 0873-SK-805 REV 01 - Wikinson Eyre 25|03|2015 CRL Escalators - Permanent Condition Diagram NTS

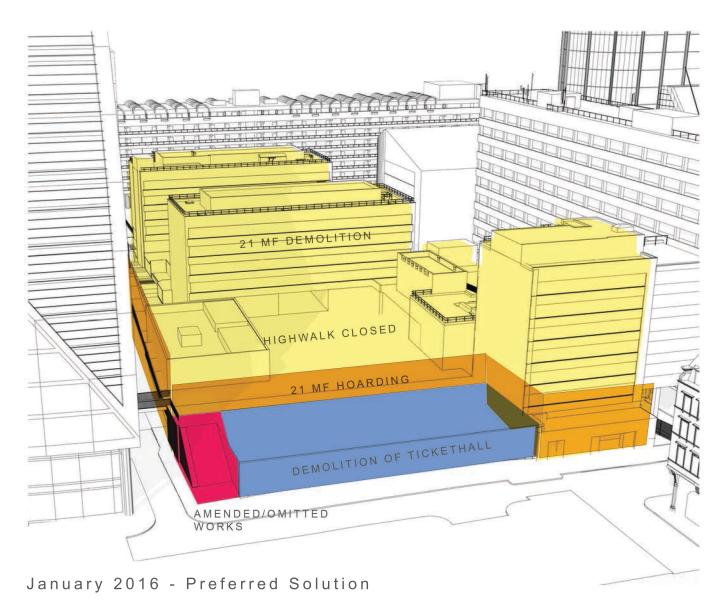

- 1) Escalators, cladding and canopy omitted from Crossrail scope of works
- 2) Cost of omitted works transferred to LS
- 3) Obligation to CoL to provide escalators transferred to LS
- 4) Crossrail ticket hall and existing highwalk demolition timing not restricted by commissioning of escalators
- 5) 21 MF hoarding up + Demolition in progress HIGHWALK CLOSED


Implications

- A) Area of works omitted or amended suitably waterproofed and protected for the duration of the project construction
- B) Escalators can be redesigned to suit permanent condition levels, spec and aesthetic requirements
- C) Warranty period for escalators commences at project completion when new highwalk opens

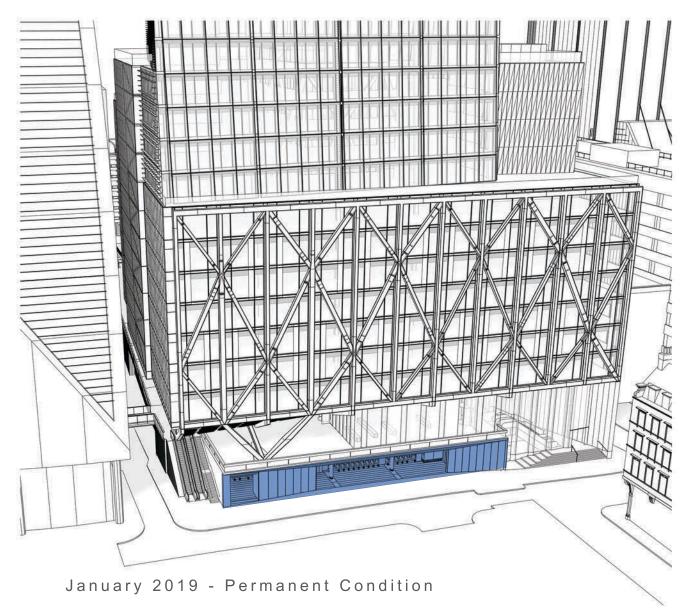

- 21 Moorfields and Crossrail Ticket Hall completed
 Escalators installed + commissioned to correct levels, spec and aesthetic quality
- 3) New Highwalk opens

21 Moorfields - 0873-SK-806 - Wikinson Eyre
10 | 02 | 2015 CRL Escalators - Permanent Condition Diagram

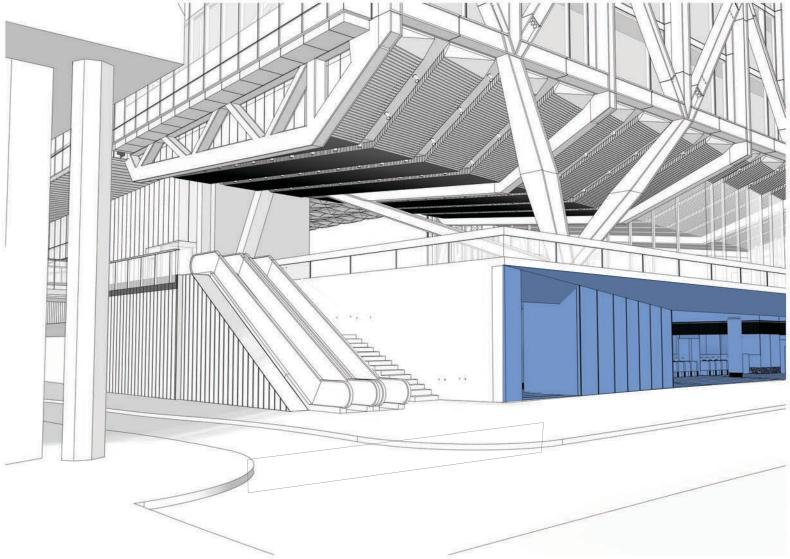

January 2019 - Permanent Condition

- Visually high quality escalators that provide an appropriate connection to the Highwalk
 Good sight lines to new retail arcade and reception areas are established, an important aspect which is critical to the success of the development
