


PLANNING AND TRANSPORTATION COMMITTEE REPORT 27/06/2020 – 21/08/2020

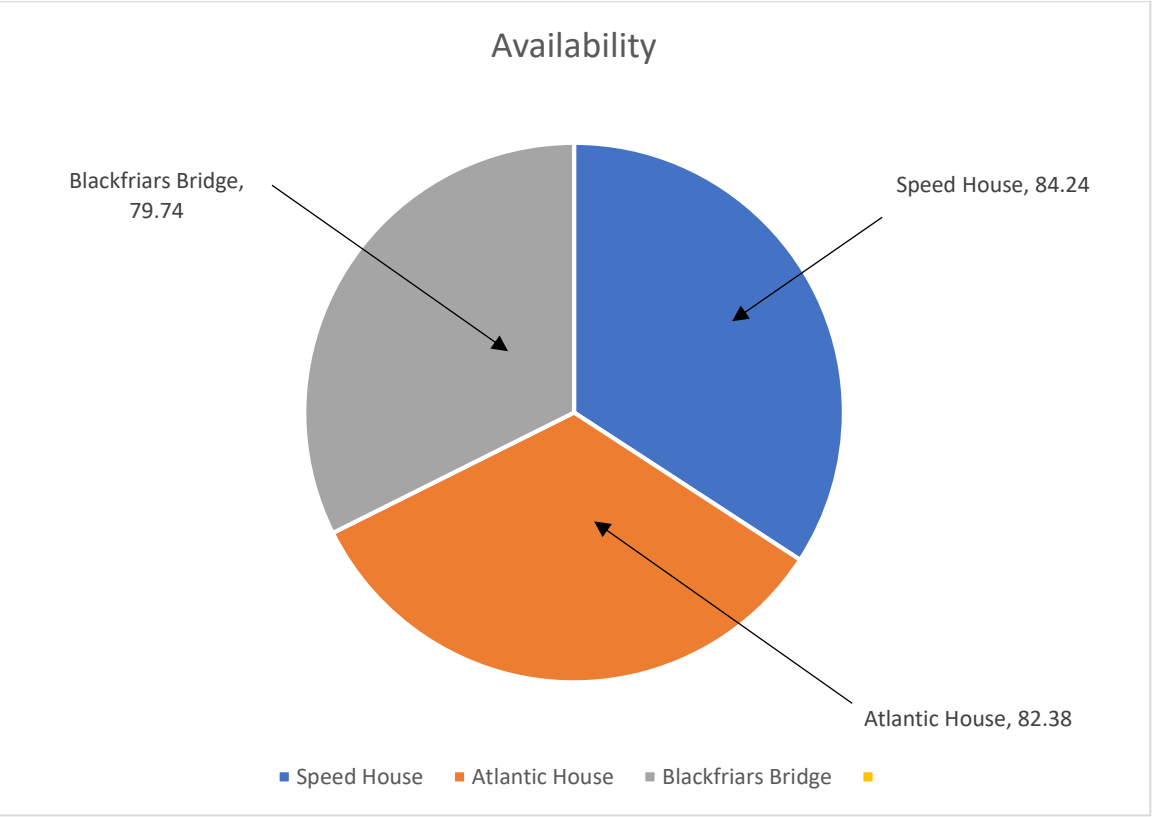

Code	Name	Time OOS	Availability
0924	Duchess Walk Public Lift LIFT CL24	55 23:59	100%
0945	London Wall Up Escalator SC6458959	55 23:59	100%
0001	Little Britain SC6458967	55 23:59	100%
7960	London Wall West SC6458965	55 23:59	100%
7963	London Wall East SC6458964	55 23:59	100%
0929	Millenium Bridge Inclinor SC6459245	55 23:59	100%
0976	Pilgrim Street SC6458969	55 23:59	100%
7999	Tower Place Scenic Lift SC6458963	55 23:59	100%
7998	Tower Place Public Lift SC6458962	55 23:59	100%
7730	Wood Street Public Lift SC6458970	0 06:43	99.50%
7740	Moor House SC6458968	19 02:00	99.23%
0916	Glass South Tower SC6459244	0 20:00	98.51%
0944	London Wall Down Escalator SC6458958	1 13:50	97.18%
7997	33 King Williams Street SC6462850	1 21:48	96.59%
7345	Speed House Public Lift SC6459146	11 10:10	84.24%
0978	Atlantic House SC6458966	9 20:48	82.38%
7964	Blackfriars Bridge SC6462771	34 20:28	79.74%

Points to Note:

- There are 17 Public Lifts/Escalators in the City of London estate. The report below contains details of the 3- public escalator/lifts that were out of service more than 95% of the time.
- The report was created on 24 August 2020 and subsequently since this time the public lifts or escalators may have experienced further breakdowns which will be conveyed in the next report.

PLANNING AND TRANSPORTATION COMMITTEE REPORT 27/06/2020 – 21/08/2020

Location	Status as of 21/08/2020	% of time in service Between 27/06/2020 and 21/08/2020	Number of times reported Between 27/06/2020 and 21/08/2020	Period of time Not in Use Between 27/06/2020 and 21/08/2020	Comments Where the service is less than 95%
Blackfriars Bridge SC6462771	In service	79.74%	1	275 hours	Due to door performance issues the lift has been isolated at weekends to avoid unnecessary trap-ins. A wider Project is due to commence in September and these works when completed will enable the lift to be brought fully back into service.
Speed House Public Lift SC6459146	In service	84.24%	1	211 hours	Engineer attended site and found intermittent issues with the magnetic impulse interference within the lift shaft sensor. Engineer repositioned sensor resolving the issue and the lift is now back in service.
Atlantic House SC6458966	In service	82.38%%	1	235 hours	Engineer attended site and found a door issue which caused several faults, the door track and doors have now been realigned and the lift is back in service.
