


## PLANNING AND TRANSPORTATION COMMITTEE REPORT 04/07/2022 – 04/09/2022

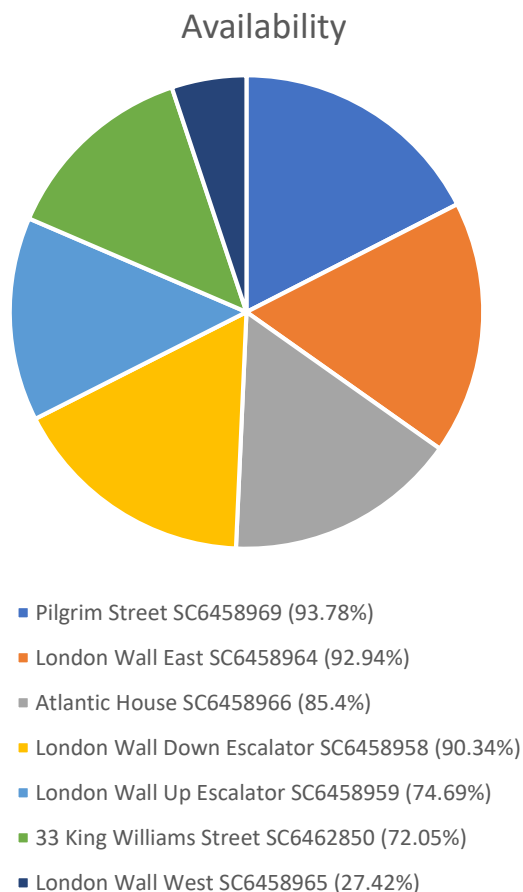

Code	Name	Time OOS	Availability
7730	Wood Street Public Lift SC6458970	0 00:00	100%
7921	Little Britain SC6458967	0 00:00	100%
	1 London Wall Lift 7	0 00:00	100%
0924	Duchess Walk Public Lift CL24	0 02:21	99.84%
0916	Glass South Tower SC6459244	0 05:52	99.61%
0931	Baynard House Car Park SC6458796	2 06:41	96.38%
7740	Moor House SC6458968	2 18:44	95.59%
7345	Speed House Glass/Public Lift SC6459146	2 19:39	95.53%
7964	Blackfriars Bridge SC6462771	3 04:50	95.16%
0976	Pilgrim Street SC6458969	3 22:03	93.78%
7963	London Wall East SC6458964	4 10:47	92.94%
0978	Atlantic House SC6458966	9 04:45	85.4%
0944	London Wall Down Escalator SC6458958	12 09:17	80.34%
0945	London Wall Up Escalator SC6458959	15 22:45	74.69%
7997	33 King Williams Street SC6462850	17 14:39	72.05%
7960	London Wall West SC6458965	45 17:26	27.42%

**Points to Note:**

- There are 16 Public Lifts/Escalators in the City of London estate. The report below contains details of the 7 - public escalators/lifts that was available less than 95% of the time.
- The report was created on 05 September 2022 and subsequently since this time the public lifts or escalators may have experienced further breakdowns which will be conveyed in the next report.

**PLANNING AND TRANSPORTATION COMMITTEE REPORT 04/07/2022 – 04/09/2022**

<b>Location</b>	<b>Status as of 04/07/2022</b>	<b>% of time in service Between 04/07/2022 and 04/09/2022</b>	<b>Number of times reported Between 04/07/2022 and 04/09/2022</b>	<b>Period of time Not in Use Between 04/07/2022 and 04/09/2022</b>	<b>Comments Where the service is less than 95%</b>
Pilgrim Street SC6458969	In service	93.78%	1	3 hours 2 minutes	Lock fault occurred was noticed on 19th August. The fault was resolved, and lift was put back in service on 20th August.
London Wall East SC6458964	In service	92.94%	1	4 hours 10 minutes	Failure over weekend, resolved on Tuesday.
Atlantic House SC6458966	Out of service	85.4%	1	9 hours 4 minutes	Out of service due to Emergency Monitoring Unit fault which needed to be sourced and replaced.
London Wall Down Escalator SC6458958	In service	80.34%	1	12 hours 9 minutes	Handrail failure. Inspection showed faults with drive tyres, handrail drive rollers and associated parts. Several days to source and repair.
London Wall Up Escalator SC6458959	In service	74.69%	1	15 hours 22 minutes	Electrical failure due to suspected water ingress. Full inspection carried out and various electrical parts replaced. Also, similar handrail failure to the Down escalator. requiring several days to source and repair.
33 King Williams Street SC6462850	In service	72.05%	3	17 hours 14 minutes	Repeated occasions where the lift doors were kept or forced open causing the lift to temporarily go out of service.
London Wall West SC6458965	Out of service	27.42%	1	45 hours 17 minutes	"Lift is stopping during travel. Initial repairs and replacement parts from Amalgamated Lifts did not resolve the issue. It requires the hydraulic equipment supplier, GS Hydraulics and the lift controller manufacture, Digital Controls to attend site at the same time.
