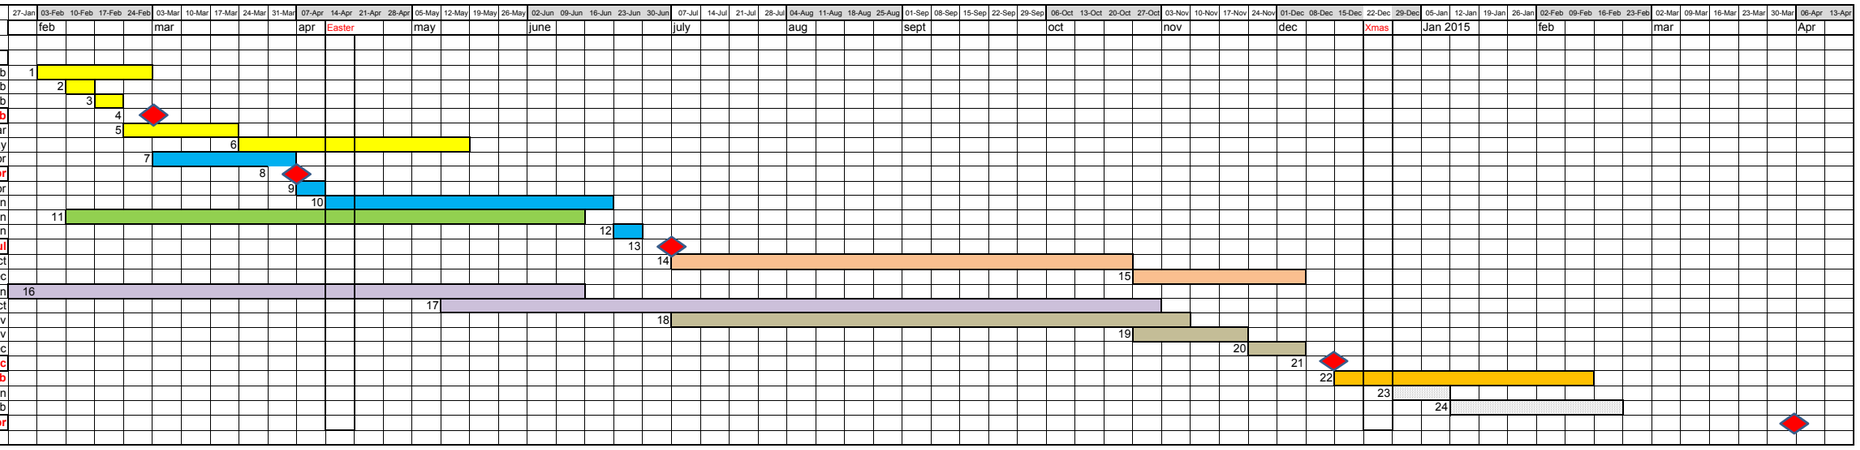HAMPSTEAD HEATH PONDS PROJECT				Week commencing	
HEADLINE PROGRAMME DATES - Agreed 26-02-2014					
Ref	Description	CoL Req't	Duration	Start	Finish
1	Finalise negotiations with Constructor			03-Feb	28-Feb
2	Agree GI specification with Constructor			10-Feb	14-Feb
3	Constructor appoints GI specialist			17-Feb	21-Feb
4	Appoint Constructor			**28-Feb**	**28-Feb**
5	Mobilise for GI			24-Feb	21-Mar
6	GI including reports			24-Mar	18-May
7	Atkins prepare Options Report			03-Mar	04-Apr
8	**Atkins submit Options Report**	**End March**		**04-Apr**	**04-Apr**
9	CoL sign off - Proceed to Planning			07-Apr	11-Apr
10	Atkins prepare Planning Application		10 weeks	14-Apr	20-Jun
11	Ditto EIA (at risk)		18 weeks	10-Feb	13-Jun
12	**City Review of Planning Application**			23-Jun	27-Jun
13	**Submit planning Application**	**End June**		**04-Jul**	**04-Jul**
14	**Planning Decision**	**Early Nov**	16 weeks	04-Jul	24-Oct
15	**JR/Standstill**	**Nov/Dec**	6 weeks	27-Oct	05-Dec
16	Atkins complete Outline Design			n/a	15-Jun
17	Atkins Detailed Design		25 weeks	12-May	31-Oct
18	Quantities for AMP exercise			07-Jul	07-Nov
19	Constructor assembles pricing			27-Oct	21-Nov
20	Negotiations on AMP			24-Nov	05-Dec
21	Agree AMP etc			**08-Dec**	**08-Dec**
22	City of London Approval Process			**08-Dec**	**13-Feb**
23	Constructor mobilisation for Site Clearance			29-Dec	11-Jan
24	**Site clearance - Scope and Period**	**Jan/Feb**		12-Jan	20-Feb
25	**Real Start on Site**	**April**		**06-Apr**	**06-Apr**
