ID	Task Mode	Task Name	Duration	Start	Finish
1		**Project Management**			
2		Project inception			
3		Gateway 1	10 days	Mon 02/11/20	Fri 13/11/20
4		**Gateway 2**			
8		Gateway 3,4	1 mon	Tue 15/03/22	Mon 11/04/22
9		Gateway 5	1 mon	Wed 08/02/23	Tue 07/03/23
10					
11		**Baseline Data**			
12		Review of existing work on Fleet Street and Temple area	11 days	Mon 04/01/21	Mon 18/01/21
13		Review of existing data within the Fleet Street and Temple area	19 days	Tue 19/01/21	Fri 12/02/21
14		**Data Collection**			
15		**Traffic Modelling Data (if required)**			
16		Data review	5 days	Mon 15/02/21	Fri 19/02/21
17		Brief development	5 days	Mon 22/02/21	Fri 26/02/21
18		Consultant procurement	5 days	Mon 01/03/21	Fri 05/03/21
19		Traffic surveys	20 days	Mon 08/03/21	Fri 02/04/21
20		**Pedestrian Modelling Data (if required)**			
28		**Stakeholder Engagement**			
34					
35		**Interactive Stakeholder Tool**			
36		Brief development	4 days	Fri 30/04/21	Wed 05/05/21
37		Consultant procurement	4 days	Wed 05/05/21	Mon 10/05/21
38		Development phase	7 days	Tue 11/05/21	Wed 19/05/21
39		Trial of interactive tool	6 days	Wed 19/05/21	Wed 26/05/21
40		Final development of interactive tool	3 days	Wed 26/05/21	Fri 28/05/21
41					
42					
43		**HSP Proposal Development**			
44		**Traffic Modelling**			
50		**Pedestrian Modelling**			
56					
57		Outline design focus and way forward	2 mons	Thu 02/12/21	Wed 26/01/22
58		G3/4 report prep	6 wks	Thu 27/01/22	Wed 09/03/22
59					
60		More detail design of inteventions	4 wks	Thu 10/03/22	Wed 06/04/22
61		**Traffic and Pedestrian Modelling Scenarios**			
62		Traffic and Pedestrian Modelling Testing	24 days	Thu 07/04/22	Tue 10/05/22

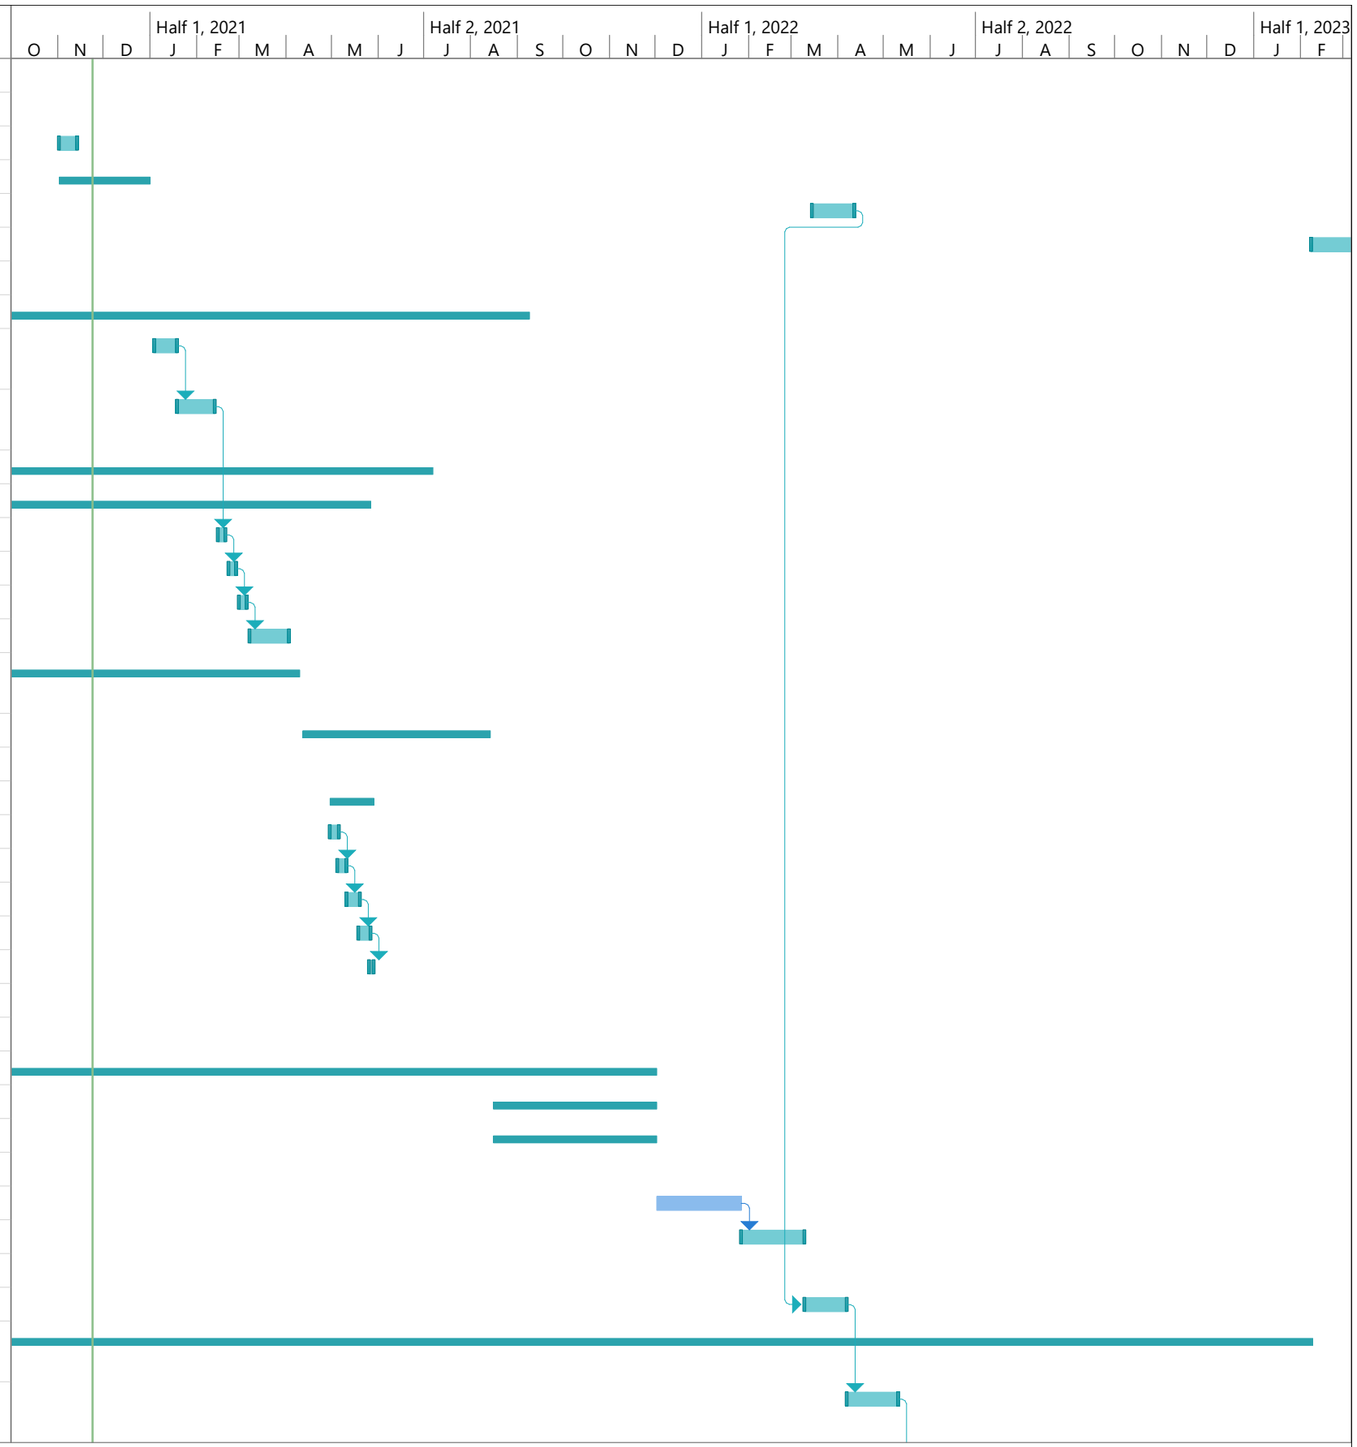

Project: Fleet Street & Temple_P
Date: Tue 24/11/20

Task	Project Summary	Manual Task	Start-only	Deadline	
Split	Inactive Task	Duration-only	Finish-only	Progress	
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress	
Summary	Inactive Summary	Manual Summary	External Milestone		

ID	Task Mode	Task Name	Duration	Start	Finish
63		Testing of traffic and pedestrian modelling scenarios	10 days	Wed 11/05/22	Tue 24/05/22
64		Verify feasibility of scenarios	10 days	Wed 25/05/22	Tue 07/06/22
65					
66		**Stakeholder Consultation on Scenarios**			
67		Preparation for stakeholder consultation (i.e. drop-in session, etc.)	10 days	Wed 08/06/22	Tue 21/06/22
68		Consultation on scenarios with Working Group	10 days	Wed 22/06/22	Tue 05/07/22
69		Consultation on scenarios with public (i.e. businesses, residents, etc.)	30 days	Wed 06/07/22	Tue 16/08/22
70		Collate stakeholder feedback on scenarios	20 days	Wed 17/08/22	Tue 13/09/22
71					
72		**Healthy Streets Plan**			
73		Assess stakeholder feedback in relations to verified scenarios	15 days	Wed 14/09/22	Tue 04/10/22
74		Incorporate stakeholder feedback into scenarios, where appropriate	25 days	Wed 05/10/22	Tue 08/11/22
75		Outline of final scenarios	14 days	Wed 09/11/22	Mon 28/11/22
76					
77		Gateway 5 prep	6 wks	Thu 29/12/22	Wed 08/02/23

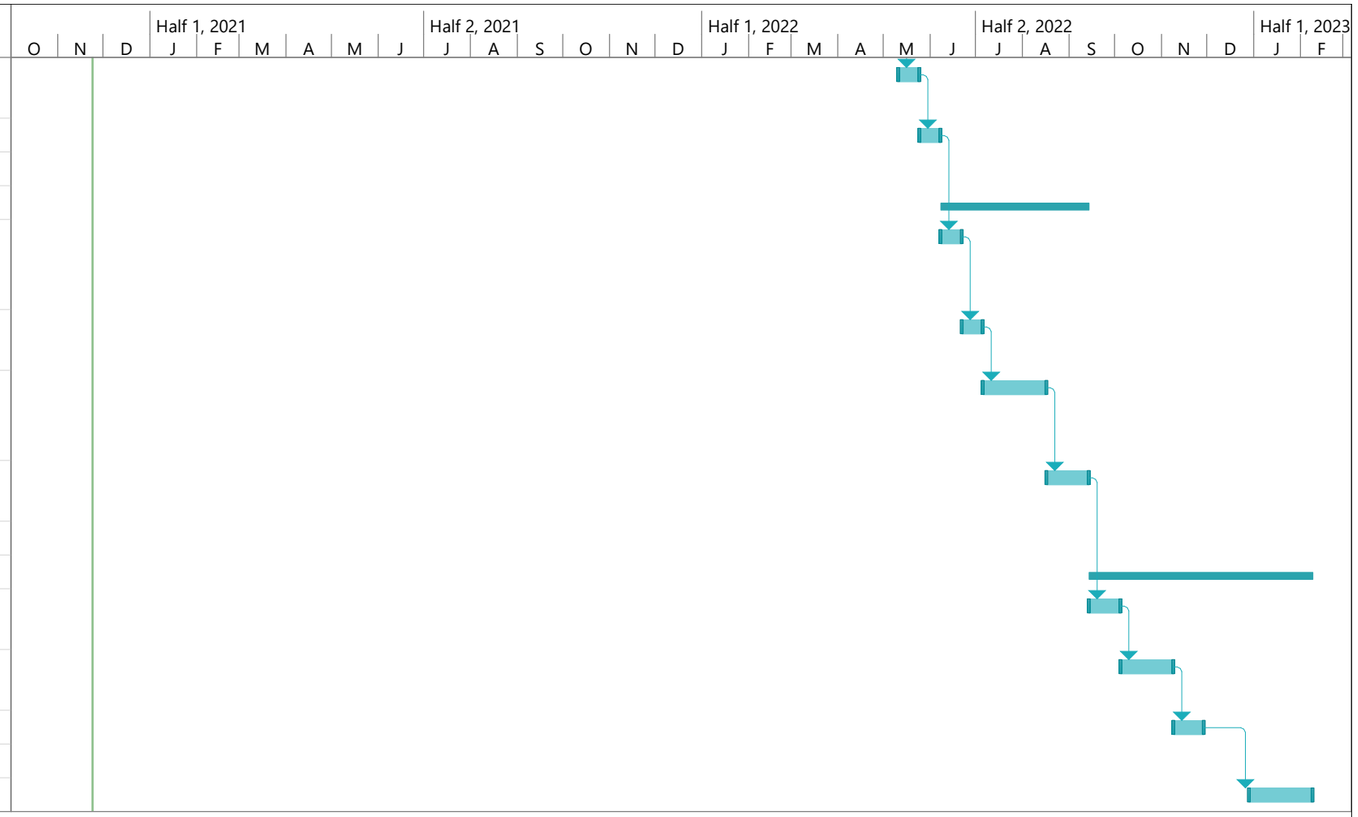

Project: Fleet Street & Temple_P
Date: Tue 24/11/20

Task	Project Summary	Manual Task	Start-only	Deadline
Split	Inactive Task	Duration-only	Finish-only	Progress
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress
Summary	Inactive Summary	Manual Summary	External Milestone	
